



## VENICE DUAL FORCE MAIN SEWER PROJECT

### Updated Schedule: Project Completion Fall/Winter 2020\*

**What is the Venice Dual Force Main (VDFM) Sewer Project?** The construction of a new 54-inch diameter force main sewer line to operate as a parallel system in conjunction with the existing sewer line. The project will create pipeline redundancy and allow for maintenance.

#### Anticipated completion dates by location:

##### Venice

- 2/1/2020 Hurricane Street at Canal Court
- 5/1/2020 Marquesas Way at Via Dolce


##### Marina del Rey

- 5/1/2020 Via Marina at Marquesas Way
- 5/1/2020 Via Marina at Tahiti Way
- 5/1/2020 Via Marina at Northwest Passage
- 11/1/2020 County Beach Lot #13 along Via Marina at Old Harbor Lane

##### Playa del Rey

- 11/1/2020 Pacific Avenue at 62nd Avenue; Tunneling activity to begin approximately 2/1/2020
- 4/1/2020 Pacific Avenue between Convoy Street and Culver Boulevard
- 9/1/2020 Pacific Avenue at Vista del Mar
- 12/1/2020 Vista del Mar at Waterview Street

\* Schedule is subject to change due to weather and other unforeseen circumstances.

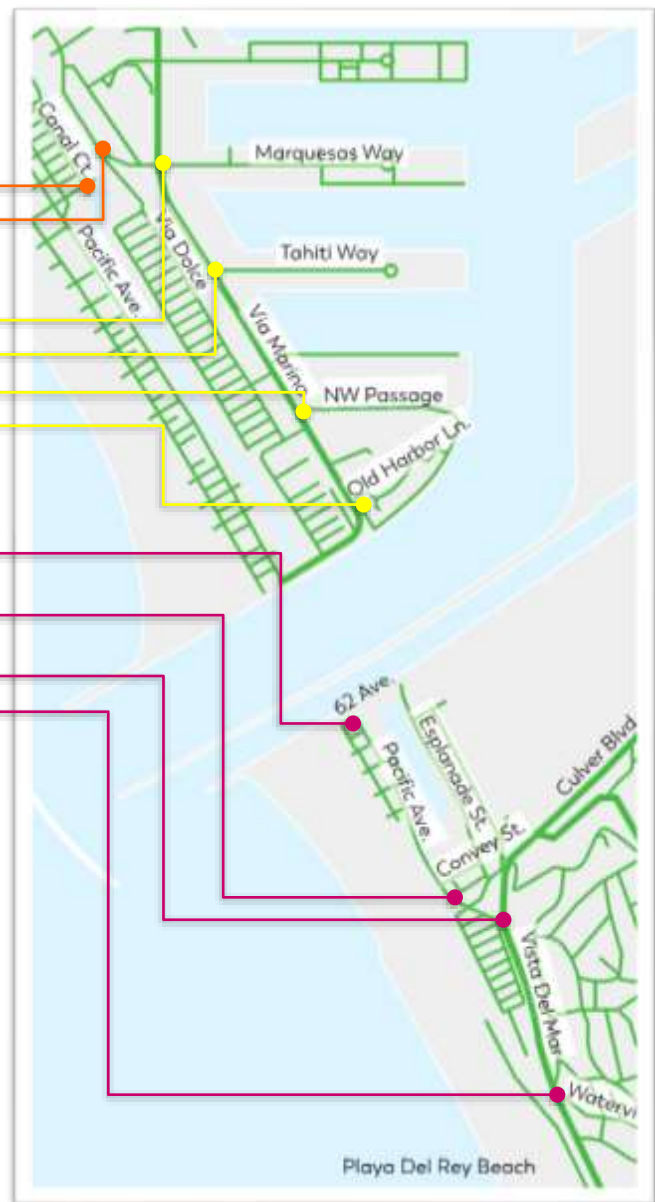

#### VDFM SEWER PROJECT OUTREACH TEAM

Tonya Durrell at (213) 485-3221 or [Tonya.Durrell@lacity.org](mailto:Tonya.Durrell@lacity.org)

After 5:00 p.m. and weekends, LA Sanitation & Environment Customer Care Center: **(800) 773-2489**

Facebook: [www.facebook.com/lacitysan/](https://www.facebook.com/lacitysan/)

Website: [www.lacitysan.org/vdfm](http://www.lacitysan.org/vdfm)





## **VENICE DUAL FORCE MAIN SEWER PROJECT** Completed Construction

### **Shaft Construction:**

- Construction of all shafts (access points) for the project has been completed at this time; this includes all project locations in Venice, Marina del Rey, and Playa del Rey
- Access points are constructed to allow for lowering and launching of the micro tunnel boring machine which creates the tunnel for installation of the sewer pipe segments

### **Tunneling and Sewer Pipe Installation:**

- Micro tunneling and installation of sewer pipe segments has been completed at the following shaft locations:
- **Shaft 1-2:** Shaft 1 (Pacific Avenue at Vista del Mar) to Shaft 2 (Pacific Avenue at Culver Boulevard/Convoy Street)
- **Shaft 5-6:** Shaft 5 (County Beach Parking Lot #13 along Via Marina at Old Harbor Lane) to Shaft 6 (Via Marina at Northwest Passage)
- **Shaft 6-8:** Shaft 6 (Via Marina at Northwest Passage) to Shaft 8 (Via Marina at Tahiti Way)
- **Shaft 9-10:** Shaft 9 (Via Marina at Marquesas Way) to Shaft 10 (Marquesas Way at Via Dolce)
- **Shaft 10-11:** Shaft 10 (Marquesas Way at Via Dolce) to Shaft 11 (Hurricane Street at Canal Court)

At the above noted locations while shaft construction, tunneling, and pipe installation is finished, crews are still conducting tasks related to fully completing these pipeline segments.

### **Shaft 11 (Hurricane Street at Canal Court):**

#### **ALL CONSTRUCTION ACTIVITY HAS BEEN COMPLETED**

- Construction of the shaft as well as all tunneling and sewer pipeline installation has been completed
- Demobilization (move-out activities), including removal of equipment and sound walls as the contractor vacates the construction work area, will be completed November 27, 2019

### **Venice Pumping Plant Generator Replacement Project:**

- The generator replacement project is anticipated to be completed in late December 2019
- Remaining activities will mainly occur within the plant, with the exception of some deliveries and demobilization activities

