


CITY OF LOS ANGELES AB 939 YEAR 2000 REPORT - PROJECT SCHEDULE

ID	Task Name	Duration	Start	Finish	Sep '0	Oct '0	Nov '0	Dec '0	Jan '1	Feb '1	Mar '1	Apr '1	May '1	Jun '1	Jul '1	Aug '1	Sep '1	Oct '1	Nov '1	Dec '1	Jan '2	Feb '2	Mar '2	Apr '2	May '2			
1	Sub-Project I - Waste Characterization	52.4 wks	09/07/00	09/07/01																								
2	Project Kick-off	1 day	09/07/00	09/07/00																								
3	Generator Selection	22.8 wks	09/19/00	02/23/01																								
4	Prepare Business Data	6.8 wks	09/19/00	11/03/00																								
10	Send Letter	22.8 wks	09/19/00	02/23/01																								
16	Database Development	4.4 wks	09/19/00	10/18/00																								
28	Generator Recruitment	20.4 wks	10/26/00	03/16/01																								
33	Training	12.6 wks	11/06/00	01/31/01																								
36	Sample Collection	34 wks	11/06/00	06/29/01																								
37	Generator Sample Collection	34 wks	11/06/00	06/29/01																								
46	Sorting	34.8 wks	11/08/00	07/09/01																								
47	Generator Sorting	33.6 wks	11/08/00	06/29/01																								
54	Diposal Site Sorting	25 wks	01/16/01	07/09/01																								
58	Draft Data of Both Sorts to City	6.7 wks	07/10/01	08/24/01																								
59	Submit Data to Other Subprojects for Incorpo	1 day	03/30/01	03/30/01																								
60	Prepare and Submit Final Report	2 wks	08/27/01	09/07/01																								
61	Sub-Project III - Targeted Generator Survey	36.8 wks	09/12/00	05/25/01																								
62	Develop Target Business List	2 wks	10/09/00	10/20/00																								
63	Draft Survey Instrument	2 wks	12/07/00	12/20/00																								
64	Final Survey Instrument	1 wk	12/21/00	12/27/00																								
65	Conduct Recruitment and Survey Calls	12 wks	01/02/01	03/26/01																								
66	Database Design/Data Entry	23 wks	09/12/00	02/19/01																								
67	Submit Data to Other Subprojects for Incorpo	1 day	03/30/01	03/30/01																								
68	Prepare and Submit Draft Report	4 wks	04/02/01	04/27/01																								
69	Prepare and Submit Final Report	4 wks	04/30/01	05/25/01																								
70	Sub-Project VI - Waste Audits	30.8 wks	09/07/00	04/10/01																								
71	Develop & Submit Waste Audit Form	2 wks	09/07/00	09/20/00																								
72	Prep. Training Mat. and Conduct Auditor Tra	4 days	09/21/00	09/26/00																								
73	Conduct On-site Waste Audits	9.8 wks	10/24/00	12/29/00																								
74	Conduct Mail Surveys	6.5 wks	10/02/00	11/15/00																								
75	Data Entry	11.2 wks	11/21/00	02/06/01																								
76	Analyze Data	2 wks	02/07/01	02/20/01																								
77	Prepare and Submit Draft Report	2 wks	02/21/01	03/06/01																								
78	Submit Data to Other Subprojects for Incorpo	1 day	03/30/01	03/30/01																								
79	City Review & Comments	3 wks	03/07/01	03/27/01																								
80	Prepare and Submit Final Report	2 wks	03/28/01	04/10/01																								


Task Report Preparation Milestone SubProject Summary

CITY OF LOS ANGELES AB 939 YEAR 2000 REPORT - PROJECT SCHEDULE

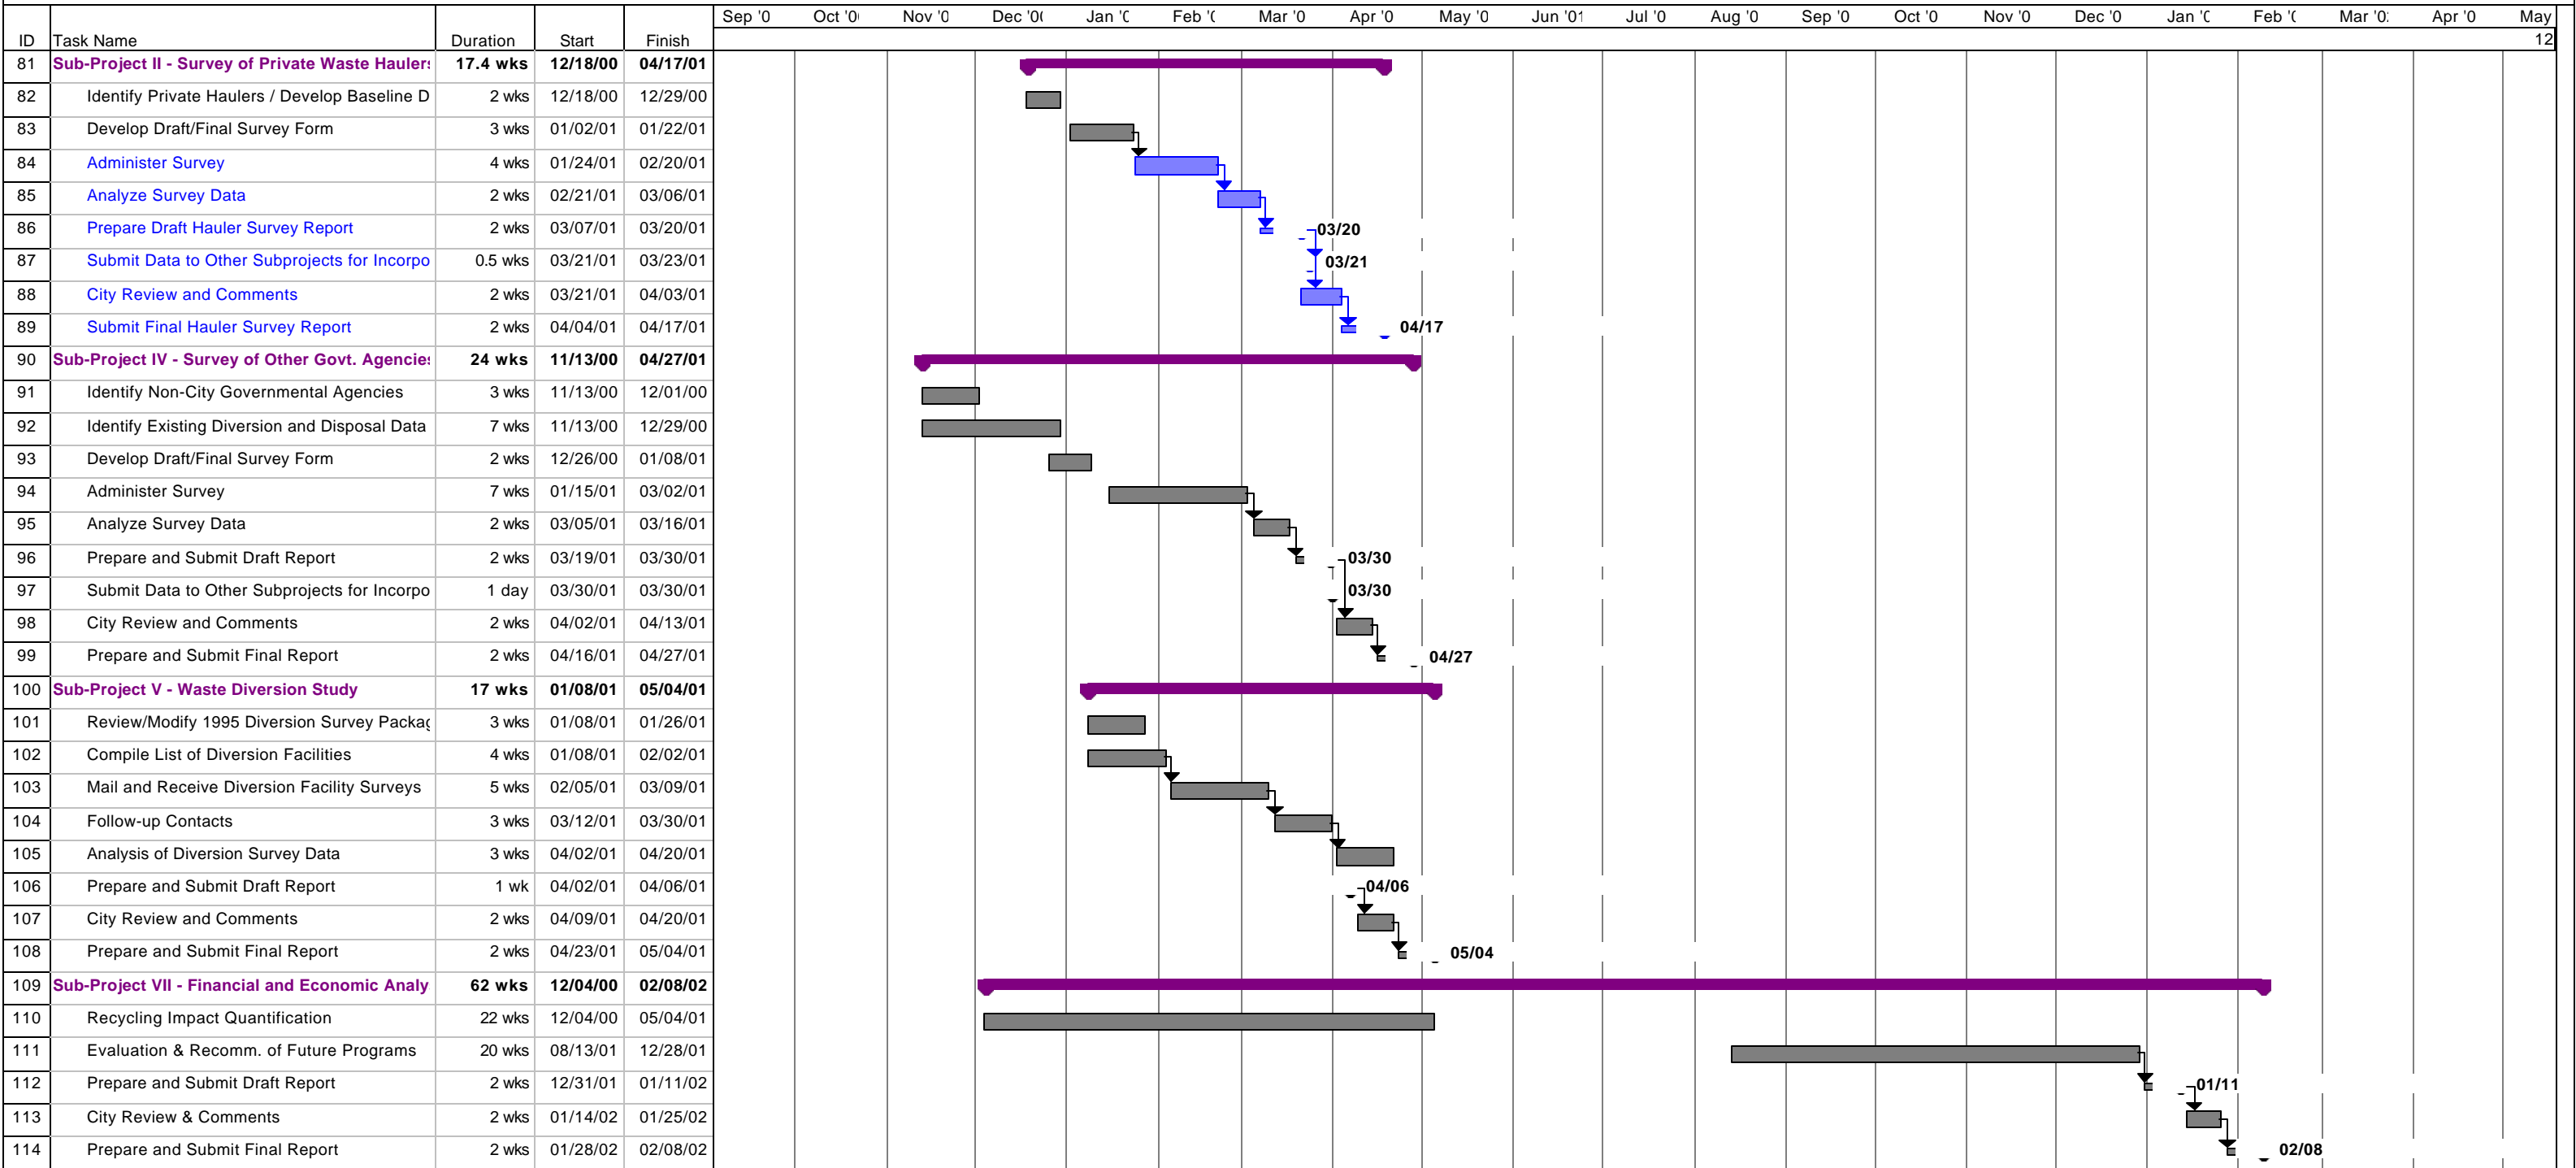

Task Report Preparation Milestone SubProject Summary

CITY OF LOS ANGELES AB 939 YEAR 2000 REPORT - PROJECT SCHEDULE

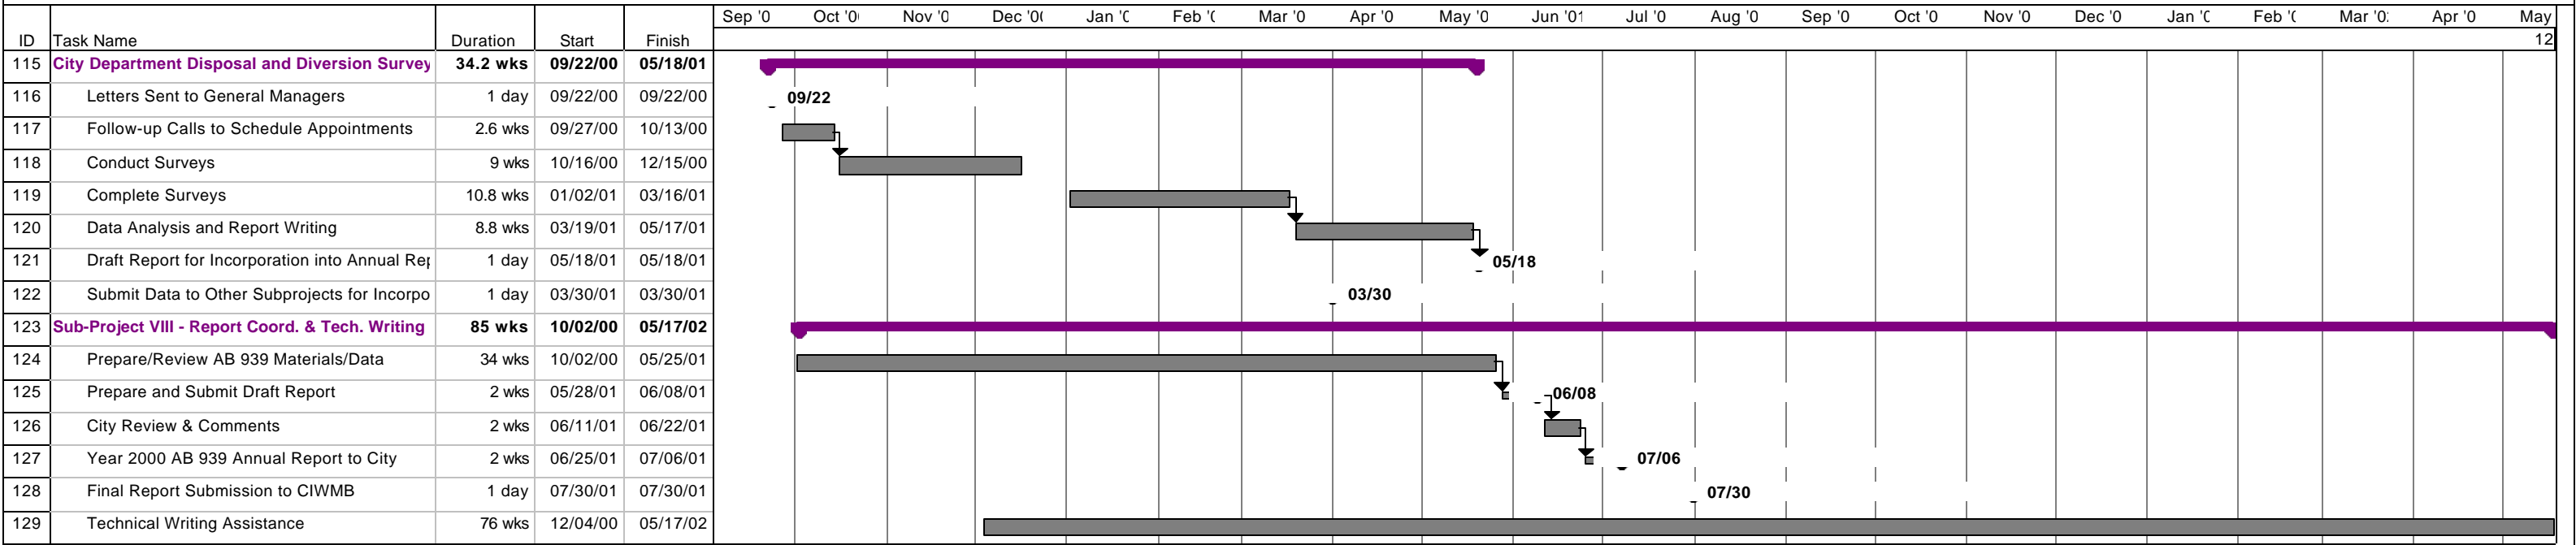

Task Report Preparation Milestone SubProject Summary
